


Project Schedule

SILICON HEARTLAND REGIONAL PROJECTS - MAINTENANCE OF TRAFFIC									
PROJ #	PID	PROJECT NAME	ALIAS	OWNER	ADVERTISE	OPEN BIDS	CONST START	OPEN TO TRAFFIC	COMPLETION
MOT DETOUR PHASE 1 (MARCH 2026 - JULY 2026)									
5	119743		SR 605 & WALNUT ST ROUNDABOUT	FRATID	7/8/2025	7/29/2025	3/2/2026	5/31/2026	10/31/2026
4	119742	DEL-CR051-2.09	COUNTY LINE & DUNCAN PLAINS ROUNDABOUT	DELTID	10/11/2025	11/4/2025	5/1/2026	7/10/2026	9/25/2026
10	119740	LICTID-CR33-0.08	DUNCAN PLAINS WEST RECONSTRUCTION	LICTID	2/11/2026	3/4/2026	5/1/2026	7/15/2026	12/31/2026
1	119726	MINK ST / DUNCAN PLAINS RD ROUNDABOUT	MINK & DUNCAN PLAINS ROUNDABOUT	LICTID	3/11/2026	4/8/2026	5/1/2026	11/1/2026	12/31/2026
MOT DETOUR PHASE 2 (AUGUST 2026 - DECEMBER 2026)									
8	119746	DEL-CR051-0.33	COUNTY LINE & FANCHER RD ROUNDABOUT	DELTID	10/11/2025	11/4/2025	7/20/2026	9/5/2026	9/25/2026
10	119740	LICTID-CR51-2.59	COUNTY LINE RD RECONSTRUCTION	LICTID	2/11/2026	3/4/2026	8/1/2026	11/15/2026	12/31/2026
1	119726	MINK ST / DUNCAN PLAINS RD ROUNDABOUT	MINK & DUNCAN PLAINS ROUNDABOUT	LICTID	3/11/2026	4/8/2026	5/1/2026	11/15/2026	12/31/2026
2	119740	LICTID-CR33-2.61	DUNCAN PLAINS CENTRAL RECONSTRUCTION	LICTID	3/11/2026	4/8/2026	8/1/2026	11/15/2026	12/31/2026
MOT DETOUR PHASE 3 (DECEMBER 2026 - JUNE 2027)									
7	119745	DEL/LIC-SR37-28.98/0.00	COUNTY LINE & SR 37 ROUNDABOUT	ODOT	8/20/2026	10/1/2026	*3/1/2027	*6/30/2027	6/30/2027
2	119740	LICTID-CR33-XXX	DUNCAN PLAINS EAST RECONSTRUCTION	LICTID	2/10/2027	3/3/2027	3/31/2027	7/16/2027	9/30/2027
1	119726		DUNCAN PLAINS EXTENSION RECONSTRUCTION	LICTID	2/10/2027	3/3/2027	3/31/2027	7/16/2027	9/30/2027
2	119740	LICTID-TR63-2.92	GREEN CHAPEL RECONSTRUCTION	LICTID	2/10/2027	3/3/2027	3/31/2027	7/16/2027	9/30/2027
MOT DETOUR PHASE 4 (AUGUST 2027-DECEMBER 2027)									
2	119740	LICTID-CR26-11.15	CLOVER VALLEY NORTH RECONSTRUCTION	LICTID	5/12/2027	6/2/2027	8/1/2027	10/31/2027	11/15/2027

*PROJECTED DATE

Project Area

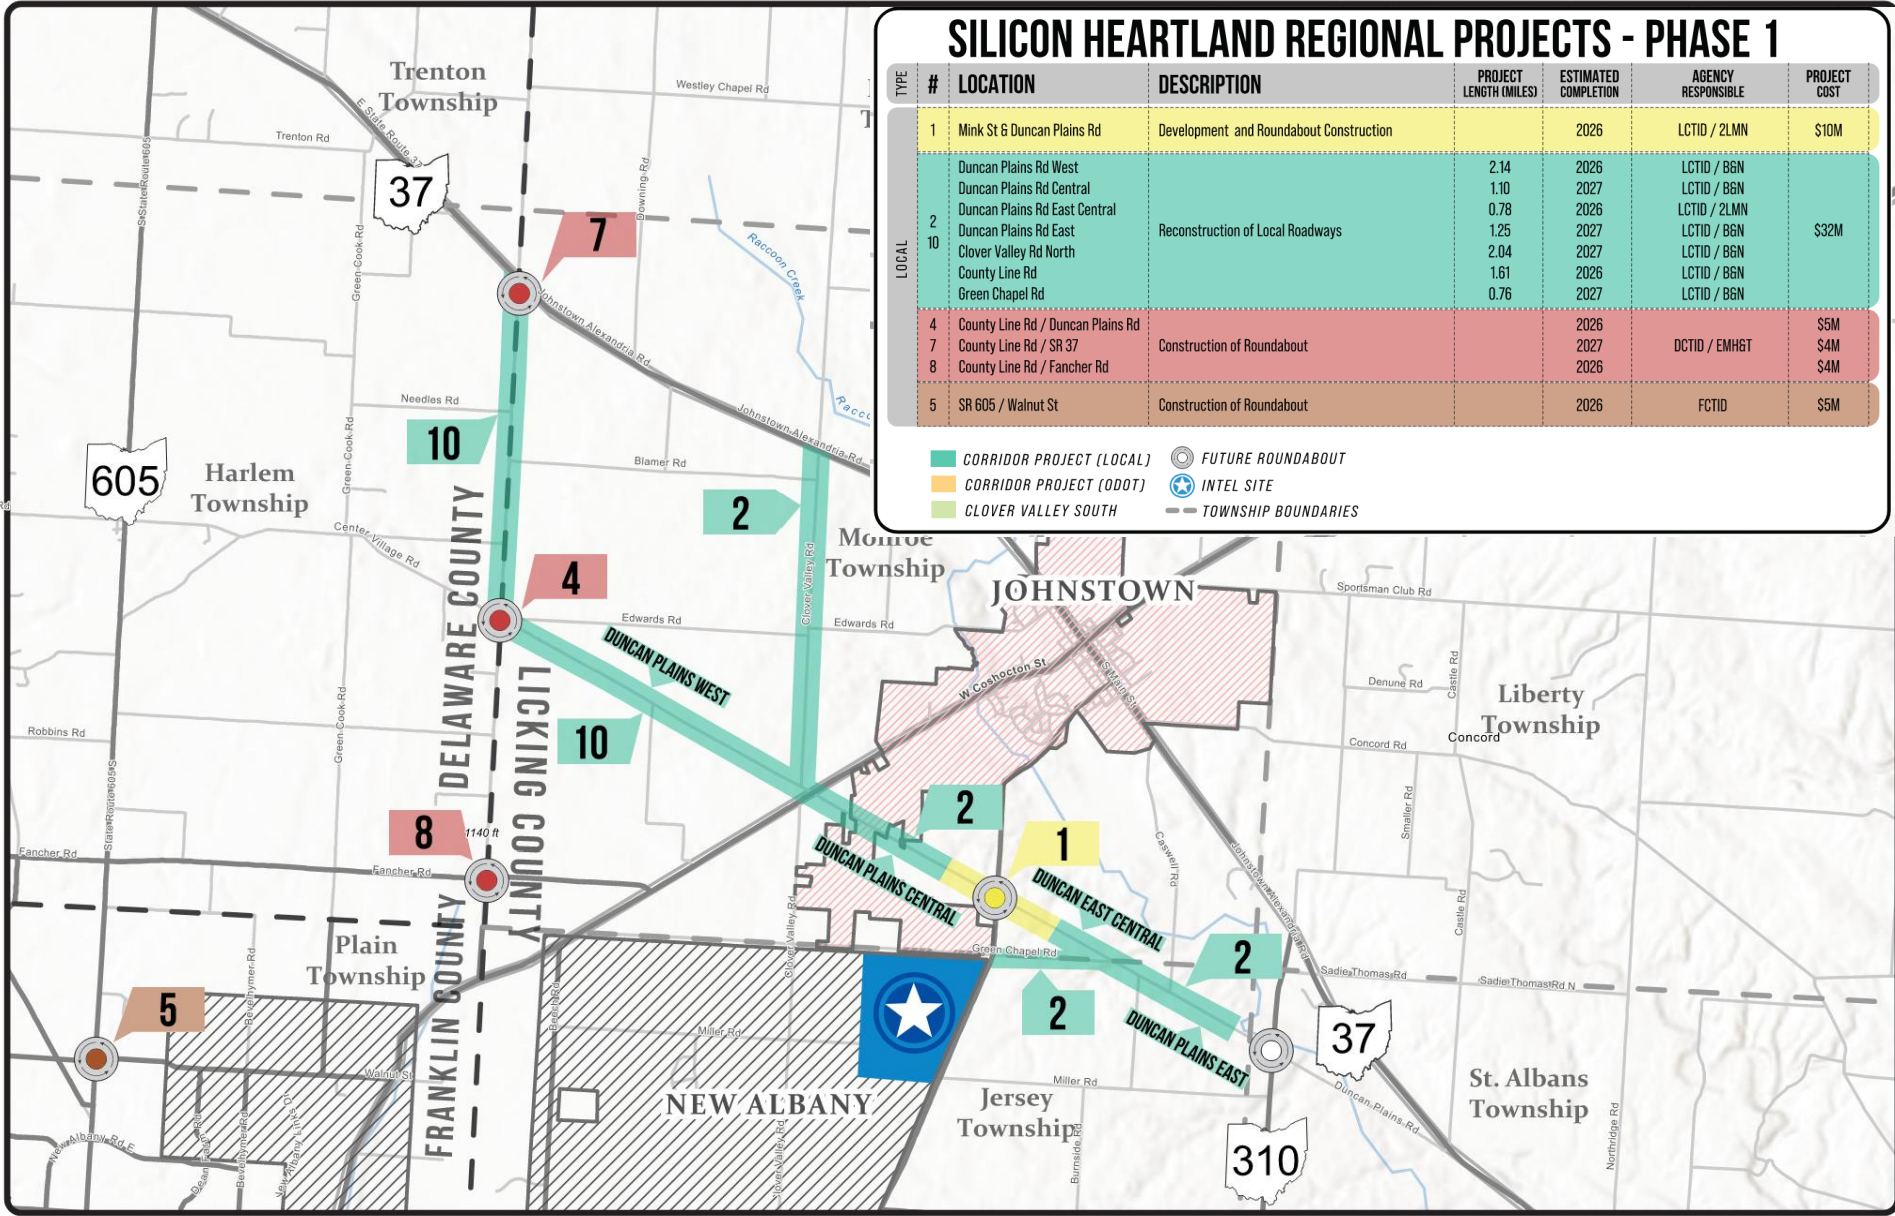

Department of
Transportation

